

Revised May 7, 2019

Both lanes from Sea Pines Circle to Office Park Rd completed on, 4/30/19 - 5/1/19  
Additional leveling at Pope Ave and Office Way to be completed by 5/9/19 - Completed - 5/7/19

Right (outside) lane from Office Park Rd to just South of Cordillo Pkwy completed on 4/30/19-5/1/19


Right (outside) lane from Executive Park Rd to Sea Pines Circle and left lane from New Orleans Rd to Sea Pines Circle completed on 5/6/19-5/7/19

Left (inside) lane from Nassau St to New Orleans Rd completed

Left (inside) lane from Office Park Rd to Nassau St completed 5/3/19-5/4/19

Right (outside) lane to be remediated & paved from Nassau St to Executive Park Rd

Paving to Occur before May 24, 2019

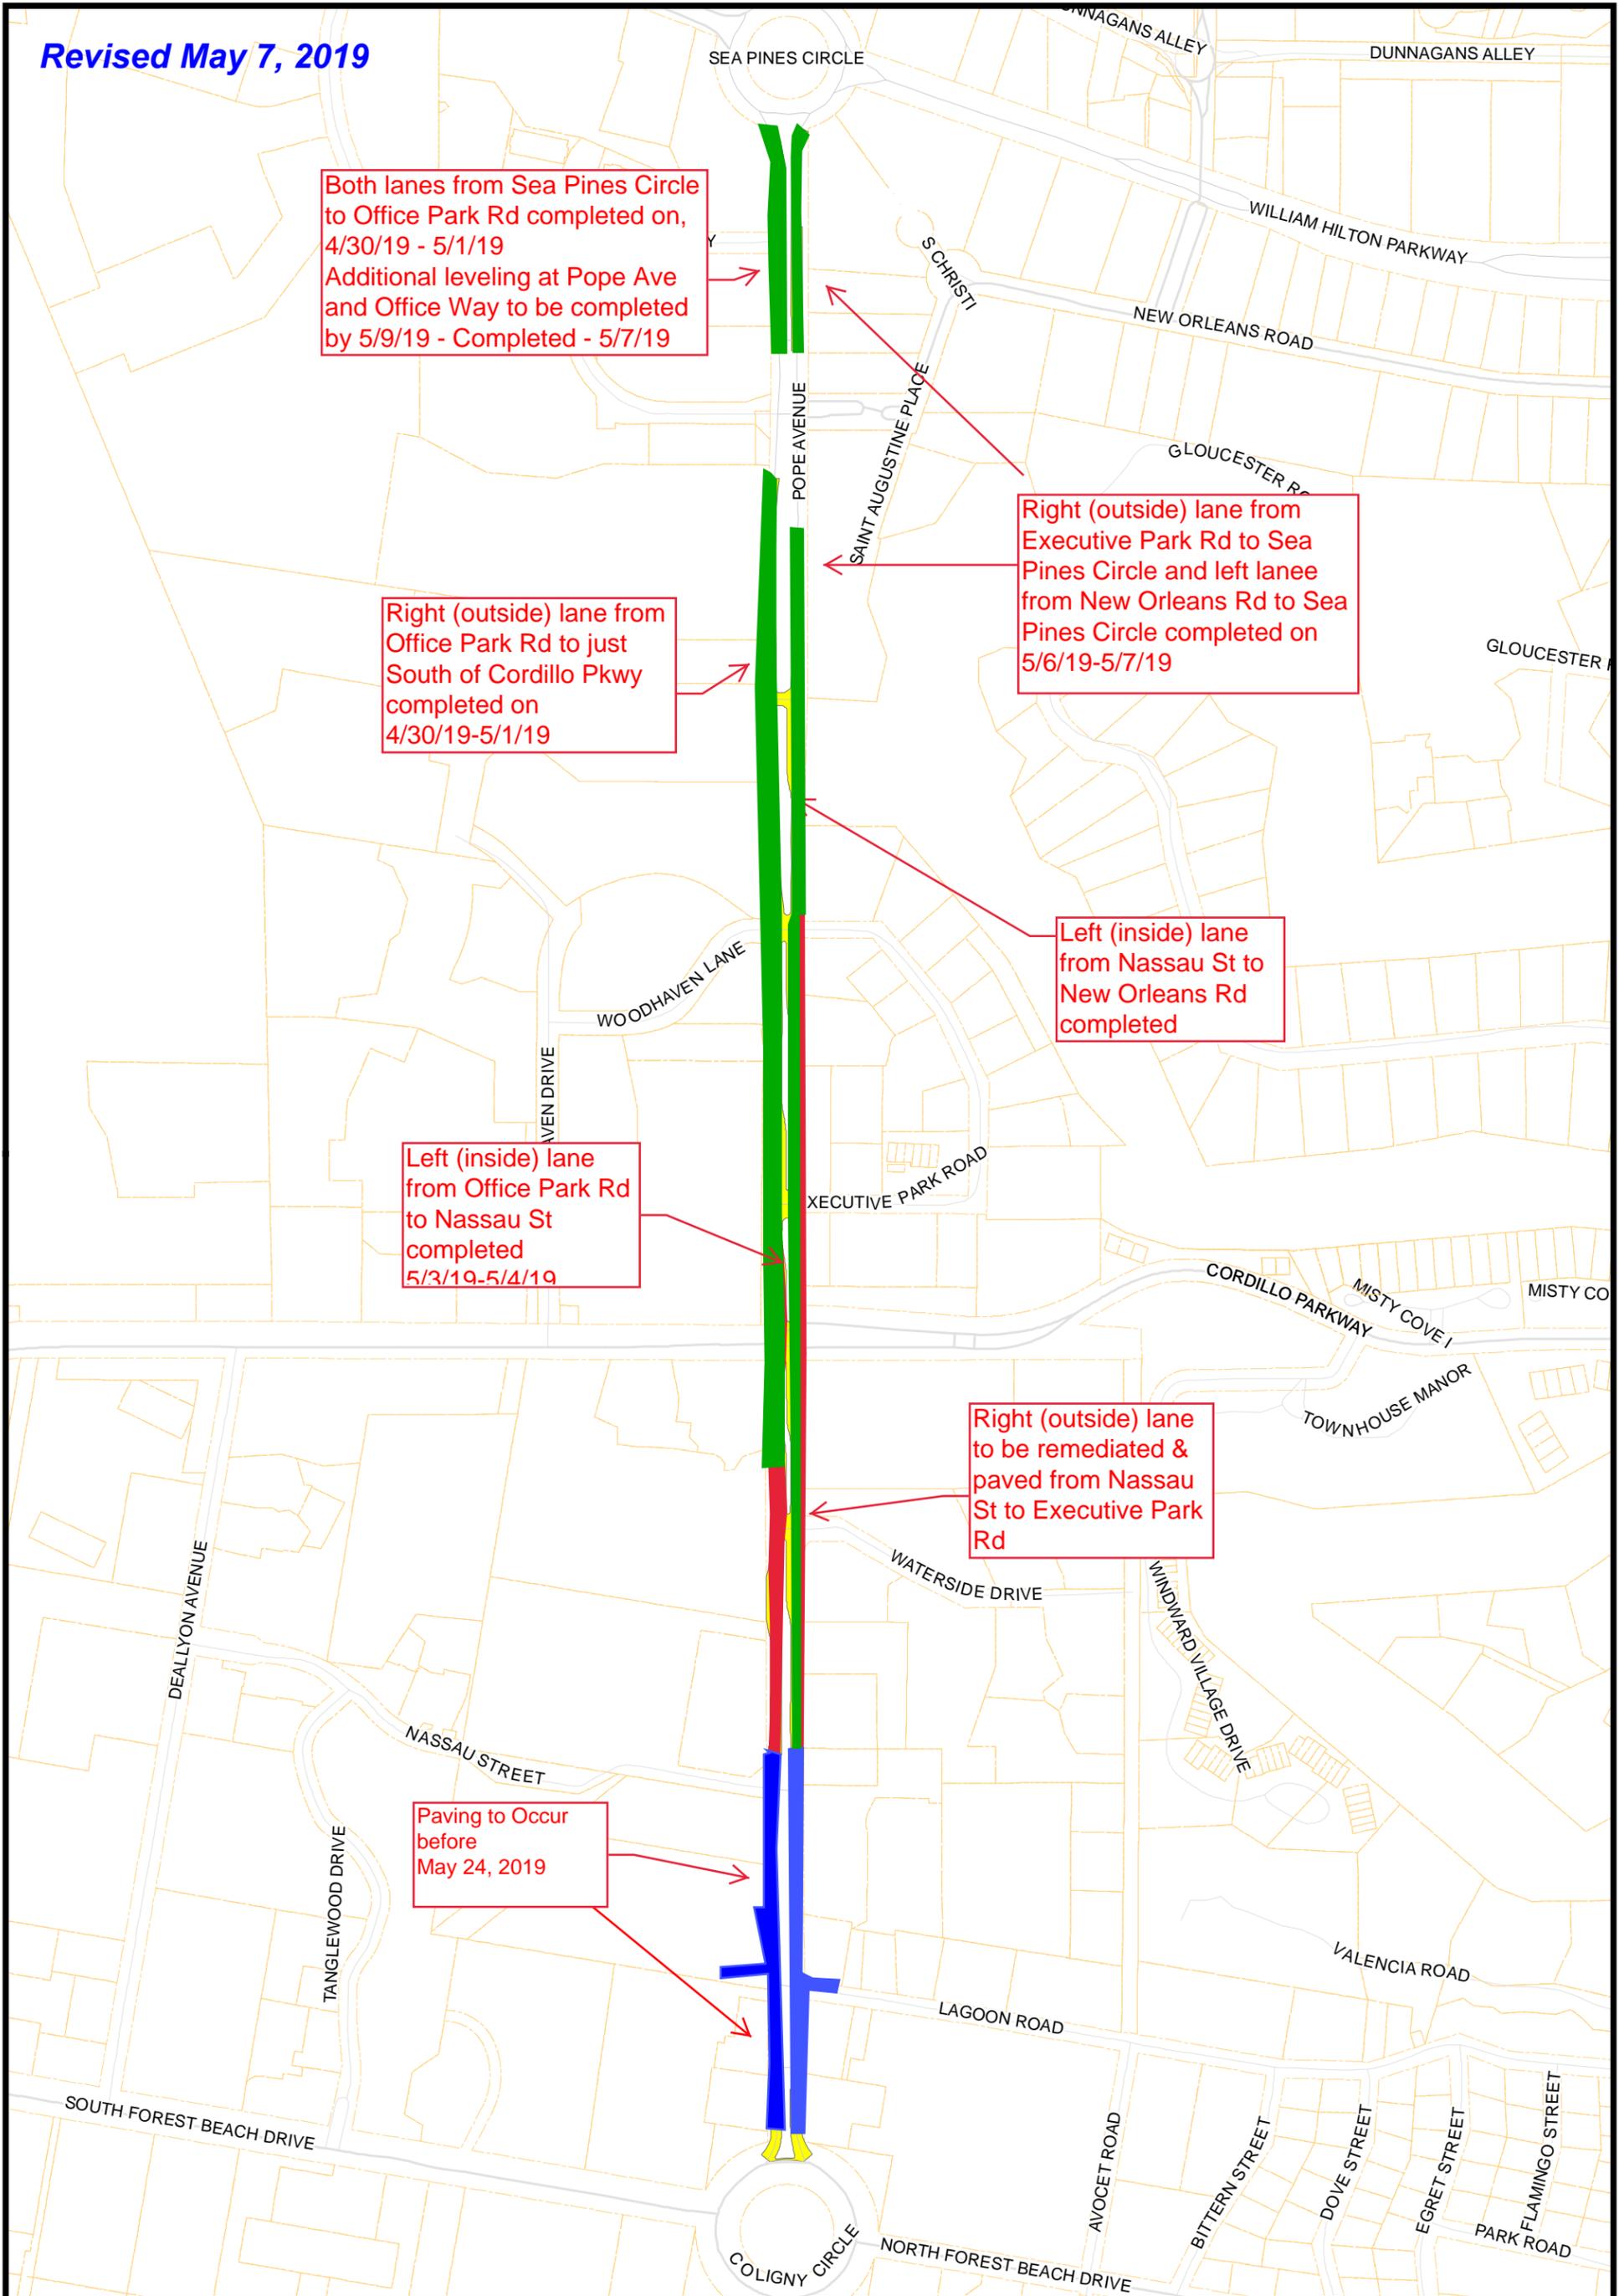

Town of Hilton Head Island  
Pope Avenue Resurfacing  
DRAFT SURFACE PAVING SCHEDULE

FOR WEEKS OF 4/29/19 - 5/9/19



TOWN OF HILTON HEAD ISLAND  
ONE TOWN CENTER COURT  
HILTON HEAD ISLAND, S.C. 29928  
PHONE (843) 341-4600  
Date Create: Monday, July 02, 2018  
Project - Pope Avenue Resurfacing\_11x17.mxd



The information on this map has been compiled from a variety of sources and is intended to be used only as a guide. It is provided without any warranty or representation as to the accuracy or completeness of the data shown. The Town of Hilton Head Island assumes no liability for its accuracy or state of completion or for any losses arising from the use of the map.
